

**Blind Pass Restoration
Weekly Progress Report
Dec. 14th thru Dec. 20th, 2008**

	Contractor: Energy Resources Inc.		
Original Contract Time:	180 days	Time Remaining:	163 days
Estimated Volume:	127,286 cyds	Volume Placed:	6,734 cyds
Required Production Rate:	740 cyds/day	Avg. Production Rate:	354 cyds/day

The following tasks were completed during the weeks of Dec. 14th thru Dec. 20th:

- The Contractor dredged an estimated 2,404 cubic yards during the reporting period. Work efficiency for the project to date is approximately 35%. Efficiency is calculated as the ratio of total dredging time to total work time.
- Dredge “Michael” commenced dredging operations on Friday, December 12th starting in Roosevelt Channel and is moving towards Blind Pass.
- The Contractor provided a partial submittal of the pre-construction surveys on Thursday, December 18th.
- The County and 3rd party turbidity monitor reviewed the sampling and reporting procedures required by contract and permit on Saturday, December 20th.
- Dredge “Nate” encountered a bearing problem with its pump on Wednesday, December 17th. Repairs are expected to be complete by Wednesday, December 31st.

The following tasks are anticipated during the week of Dec. 21st thru Dec. 27th:

- The City of Sanibel and Lee County issued an advisory noting increased shark sightings in the project area on Monday, December 22nd.
- Work should begin to construct the steel sheetpile containment cell on the seaward side of Blind Pass Bridge on Tuesday, December 23rd. The cell will be used to dewater material not allowed for beach or nearshore placement. Construction should be completed by early January.
- The Contractor is scheduled to stop operations from Thursday, December 25th thru Sunday, December 28th in observance of Christmas.

Outstanding and other Items to Note:

- The DEP, Ding Darling NWR, and Lee County will holding public meetings to discuss the proposed 474 acre Pole and Troll zone in Wulfert Flats at the following dates and locations: (Each meeting is expected to begin at 6:00 pm)
 - Monday, January 12th – Pine Island (Meeting Facility TBD)
 - Tuesday, January 13th – Sanibel Island @ Ding Darling NWR
 - Wednesday, January 14th – Ft. Myers @ Lee County Government Facility.

***The Specific meeting room locations will be provided.**
- The Contractor is anticipated to begin working night time hours by January 1, 2009 to dredge material suitable for beach placement.
- The Contractor is anticipated to install a booster pump by January 1. The pump is anticipated to work 24 hrs. Per day.



Saturday, December 20, 2008
Dredge "Michael" working in
Roosevelt Channel



Wednesday, December 17, 2008
90° Elbows Used For Placing The
Nearshore Material.




Wednesday, December 17, 2008
Beach Placement Operations

Blind Pass Maintenance Dredging Production Tracking

Contract Completion
Date: May 30, 2009

Project Volume = 127,286 cyds

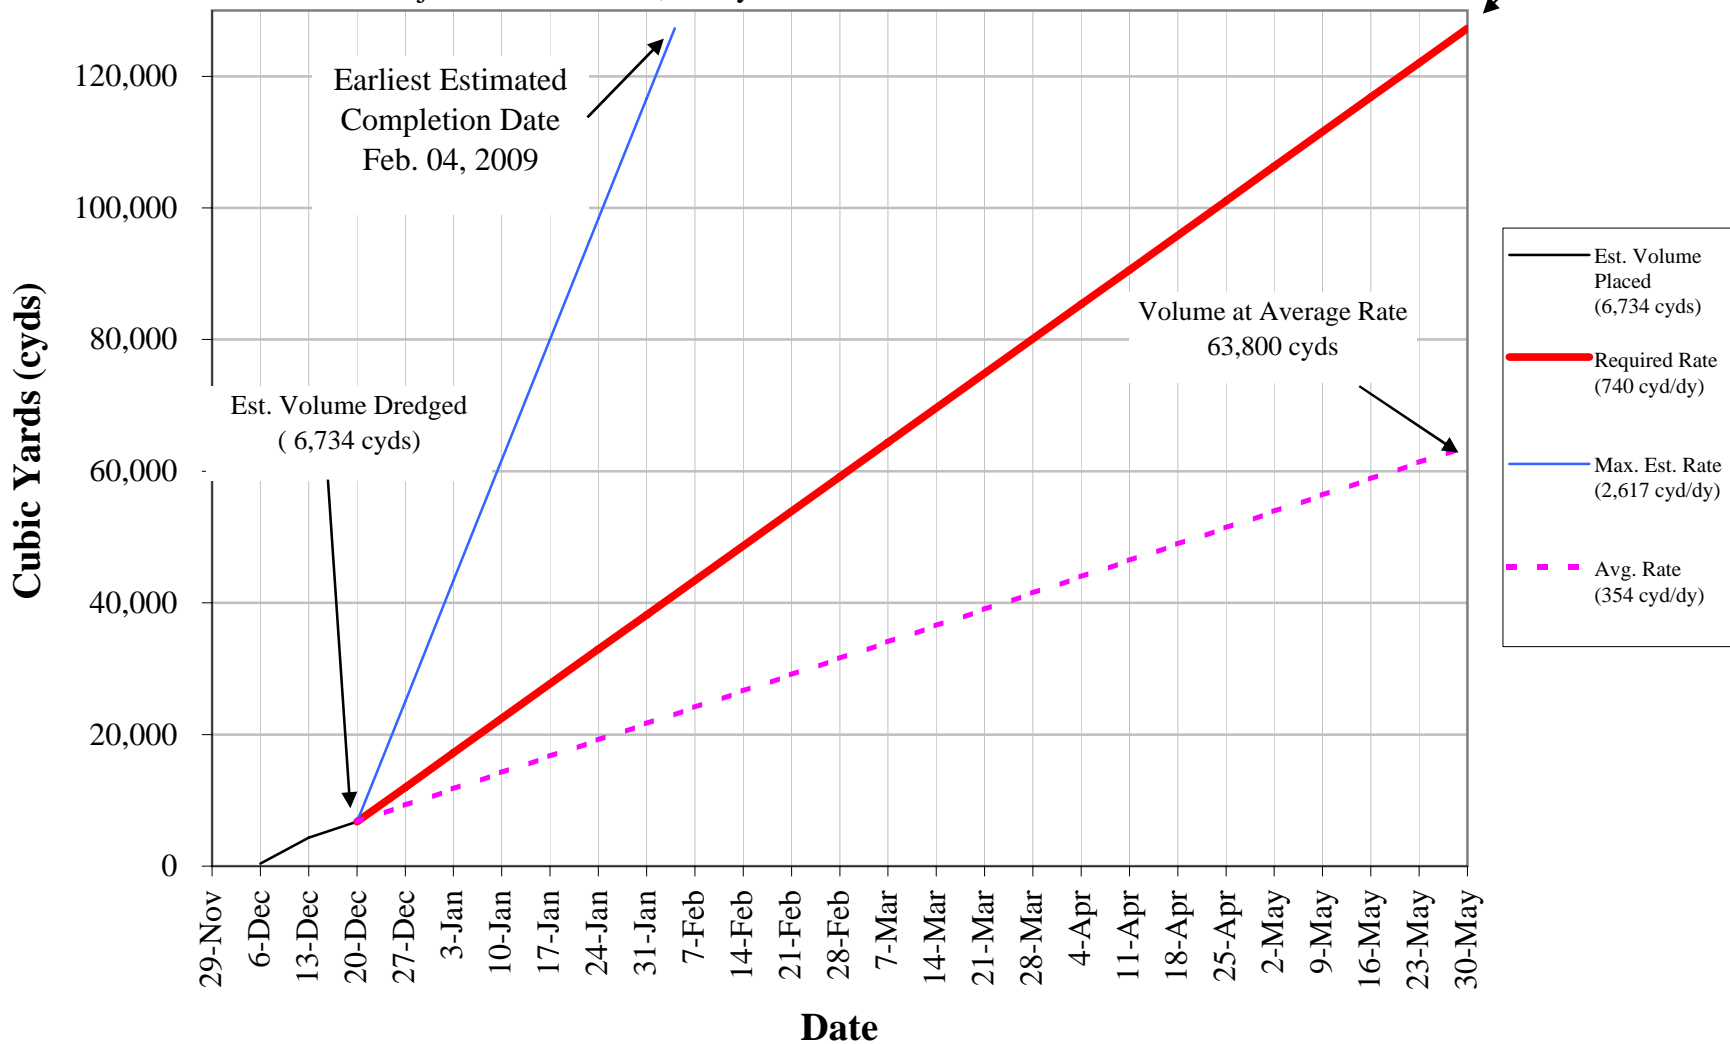



TITLE:
 BLIND PASS MAINTENANCE DREDGING
 CONSTRUCTION SCHEDULE
 WEEK OF DECEMBER 22, 2008

NATURAL RESOURCES DIV
 1500 Monroe St. Fort Myers, Florida 33901
 Ph. (239) 533-8109/10 Fax. (239) 485-8408

LEE COUNTY
 SOUTH WEST FLORIDA

LEGEND

ANTICIPATED CONSTRUCTION AREA(S) FOR THE TIMEFRAMES SHOWN ARE PROVIDED BELOW:

- PREVIOUSLY CONSTRUCTED
- 0 TO 5 DAYS
- 5 TO 15 DAYS
- 15 TO 30 DAYS

FILE: S:\NATRES\MARINE\BEACHMANAGEMENT\BLINDPASS\DRAWINGS\BLINDPASS.CONSTRUCTION.dwg
 DATE: 17-NOV-08
 DRAWN: RBN
 APPROVED: RBN

SCALE:
 1" = 400'

SHEET:
 01 OF 01
