

**Blind Pass Restoration
Weekly Progress Report
Feb. 08th thru Feb. 14th, 2009**

Contractor: Energy Resources Inc.

Original Contract Time:	180 days	Time Remaining:	104 days
Estimated Volume:	127,286 cyds	Volume Placed:	54,673 cyds
Required Production Rate:	698 cyds/day	Avg. Production Rate:	770 cyds/day

The following tasks were completed during the weeks of Feb. 08th thru Feb. 14th:

- The Contractor dredged an estimated 6,912 cubic yards during the reporting period. Work efficiency for the week was approximately 65% for a project average of 50% to date. Efficiency is calculated as the ratio of total dredging time to total work time.
- The Contractor completed operations to clear the western side of Wulfert Channel on Wednesday, February 11th.
- The Contractor submitted a revised schedule on Friday, February 13th. The schedule shows the following mile stones:
 - Estimated final completion Friday, May 28th.
 - Trucking of unsuitable material projected to occur between Saturday, April 4th, and Monday April 20th.
 - Removal of containment cell by April 11th.
- Lee County began shorebird nesting surveys on Monday, February 16th. Surveys will occur daily when the contractor is expected to work.

The following tasks are anticipated during the week of Feb. 15th thru Feb. 21st:

- The Contractor is expected conduct a pre-fill survey of the containment cell on Monday, February 16th. The survey will be used to quantify the preconstruction conditions of the cell and limit the volume of beach compatible material trucked to the upland disposal site.

Outstanding and other Items to Note:

- The Contractor is expected to move 1 dredge into the Gulf of Mexico and begin dredging operations in the seaward portion of the pass on Tuesday, February 24th.
- The Contractor is expected to move the booster pump onto the beach front on Tuesday, February 24th.
- The Contractor is expected to intermittently work night time hours while dredging the seaward portion of the channel. The booster pump is expected to be necessary during the night time operations.



Monday, February 16, 2009
Beach Fill Operations




Monday, February 09, 2009
Dredging Operations in Wulfert
Channel



Thursday, February 12, 2009
View of Containment Cell

Blind Pass Maintenance Dredging Production Tracking

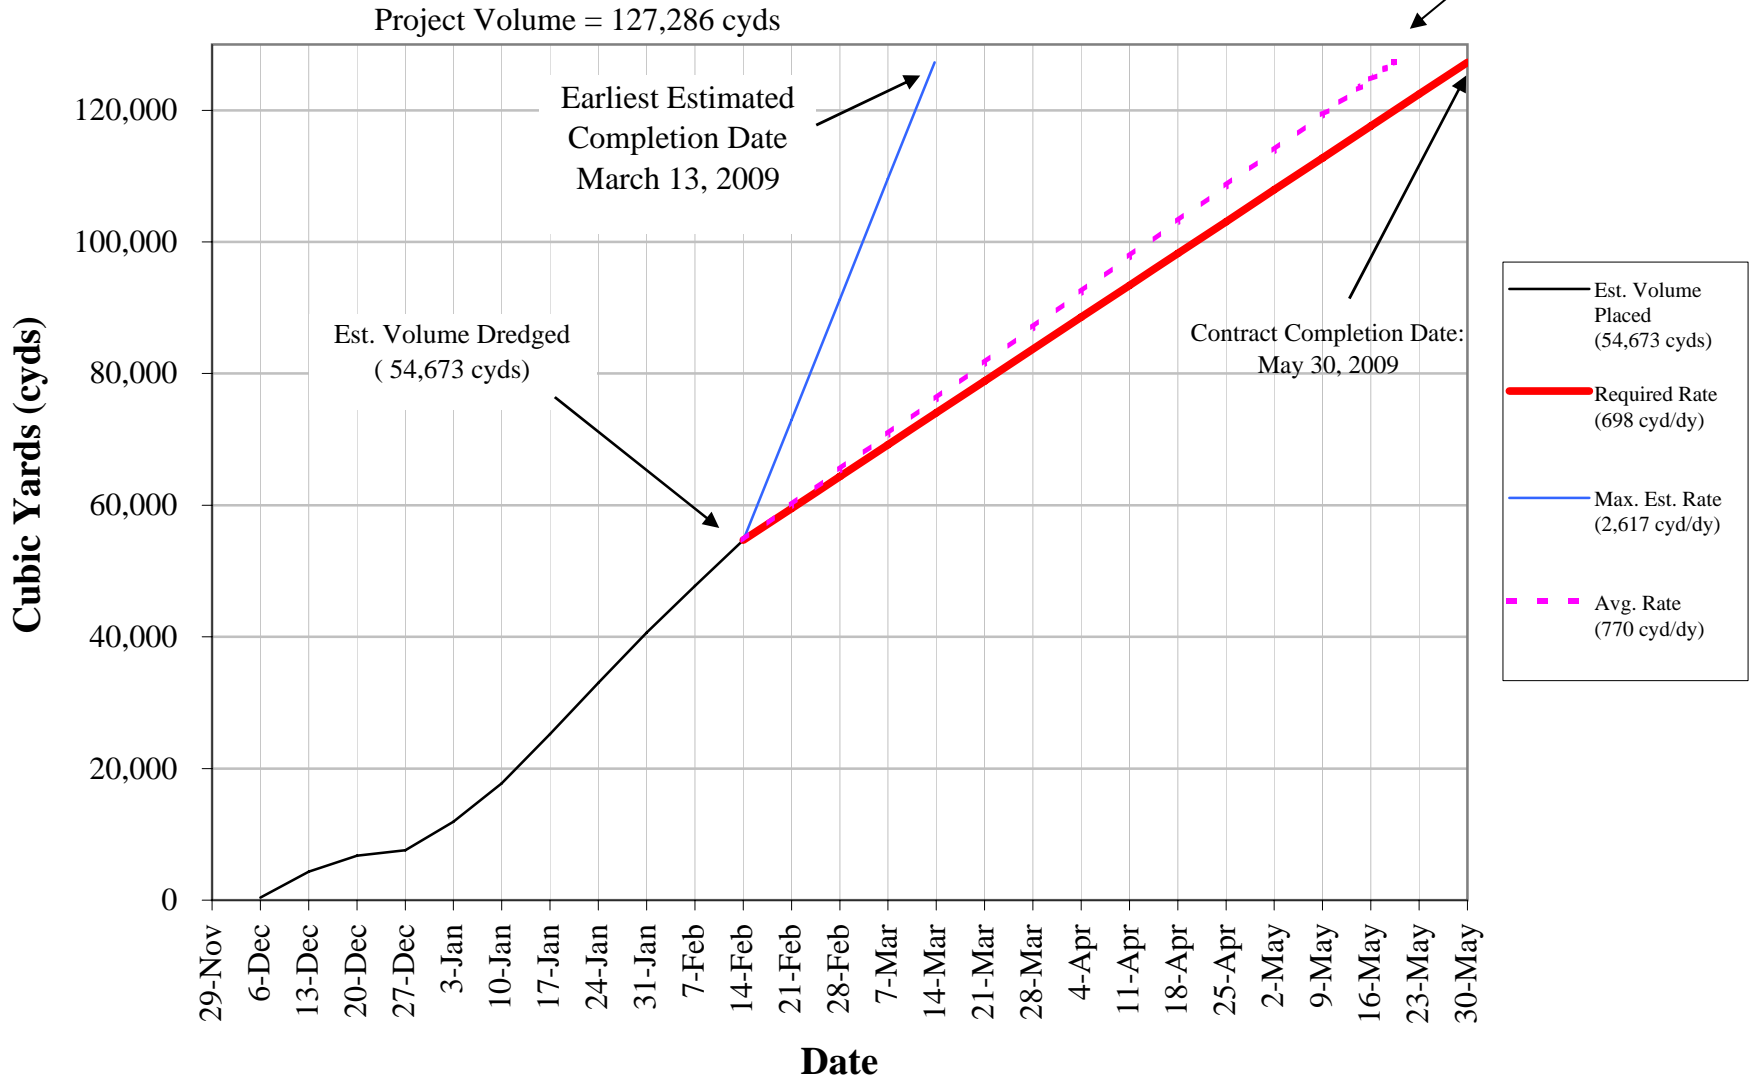



CAPTIVA ISLAND

SANIBEL ISLAND

LEGEND

ANTICIPATED CONSTRUCTION AREA(S) FOR THE TIMEFRAMES SHOWN ARE PROVIDED BELOW:

- PREVIOUSLY CONSTRUCTED
- 0 TO 5 DAYS
- 5 TO 15 DAYS
- 15 TO 30 DAYS

TITLE:
 BLIND PASS MAINTENANCE DREDGING
 CONSTRUCTION SCHEDULE
 WEEK OF FEBRUARY 17, 2009

NATURAL RESOURCES DIV
 1500 Monroe St. Fort Myers, Florida 33901
 Ph. (239) 533-8109/10 Fax. (239) 485-8408

LEE COUNTY
 SOUTH WEST FLORIDA

FILE: S:\NATRES\MARINE\BEACHMANAGEMENT\
 BLINDPASS\DRAWINGS\BLINDPASS_
 CONSTRUCTION.dwg
 DATE: 17-NOV-08
 DRAWN: RBN
 APPROVED: RBN

SCALE:
 1" = 400'
 SHEET:
 01 OF 01
